Lake City International Building-- Twin Falls, Idaho

ID	Task Name	Duration	Start	Finish
1	**Lake City International Building**	**103.33 days**	**Mon 2/12/07**	**Mon 7/23/07**
2	**GENERAL REQUIREMENTS**	**87 days**	**Mon 2/12/07**	**Tue 6/26/07**
3	Notice to Proceed	0 days	Mon 2/12/07	Mon 2/12/07
4	Mobilization, Bonds, Permits	7 days	Mon 2/12/07	Wed 2/21/07
5	Temporary Utilities	80 days	Wed 2/21/07	Tue 6/26/07
6	**EXCAVATION AND SITEWORK**	**6 days**	**Thu 2/22/07**	**Fri 3/2/07**
7	Site Layout	1 day	Thu 2/22/07	Fri 2/23/07
8	Building Pad and Fill	5 days	Fri 2/23/07	Fri 3/2/07
9	**BUILDING CONCRETE**	**19 days**	**Fri 3/2/07**	**Mon 4/2/07**
10	Reinforcing Steel and Anchor Bolts	3 days	Fri 3/2/07	Wed 3/7/07
11	Electrical Ground Wire in Footing	1 day	Wed 3/7/07	Thu 3/8/07
12	Concrete Footings	4 days	Fri 3/9/07	Thu 3/15/07
13	Concrete Foundation	4 days	Thu 3/15/07	Wed 3/21/07
14	Insulate Insulation Foundation	1 day	Wed 3/21/07	Thu 3/22/07
15	Backfill and Grading	2 days	Thu 3/22/07	Mon 3/26/07
16	Plumbing Under Slab Rough-in	2 days	Tue 3/27/07	Thu 3/29/07
17	Electrical Under Slab Rough-in	2 days	Tue 3/27/07	Thu 3/29/07
18	Fine Grade	1 day	Thu 3/29/07	Fri 3/30/07
19	Concrete Floors	1 day	Fri 3/30/07	Mon 4/2/07
20	BUILDING CONCRETE COMPLETE	0 days	Mon 4/2/07	Mon 4/2/07
21	**METAL BUILDING CONSTRUCTION**	**30 days**	**Mon 4/2/07**	**Thu 5/17/07**
22	Metal Building Package Delivery	1 day	Mon 4/2/07	Tue 4/3/07
23	Metal Building Erection	20 days	Tue 4/3/07	Thu 5/3/07
24	Construct Crane, Rails, and Mezzanine	8 days	Thu 5/3/07	Wed 5/16/07
25	Install Windows	1 day	Wed 5/16/07	Thu 5/17/07
26	BUILDING ERECTION COMPLETE	0 days	Thu 5/17/07	Thu 5/17/07
27	**BUILDING ROUGH-IN**	**9 days**	**Thu 5/17/07**	**Fri 6/1/07**
28	Install Hollow Metal Door Frames	2 days	Thu 5/17/07	Mon 5/21/07
29	Install Store Front Windows	1 day	Thu 5/17/07	Fri 5/18/07
30	Plumbing Rough-in	5 days	Thu 5/17/07	Thu 5/24/07
31	HVAC Rough-in	7 days	Thu 5/17/07	Wed 5/30/07
32	Electrical Rough-in	5 days	Thu 5/17/07	Thu 5/24/07
33	Crane Installation	2 days	Thu 5/17/07	Mon 5/21/07
34	Batt Insulation	2 days	Wed 5/30/07	Fri 6/1/07
35	BUILDING ROUGH-IN COMPLETE	0 days	Fri 6/1/07	Fri 6/1/07
36	**OUTSIDE CONSTRUCTION**	**31 days**	**Thu 5/17/07**	**Fri 7/6/07**
37	Site Drainage Systems	8 days	Thu 5/17/07	Thu 5/31/07
38	Electrical Service	3 days	Thu 5/31/07	Tue 6/5/07
39	Water and Sewer Hook-up	3 days	Thu 5/31/07	Tue 6/5/07
40	Outside Grading	5 days	Tue 6/5/07	Tue 6/12/07
41	Outside Concrete Work	8 days	Wed 6/13/07	Mon 6/25/07
42	Block Trash Enclosure	4 days	Mon 6/25/07	Mon 7/2/07
43	Fence and Trash Gate	3 days	Mon 7/2/07	Fri 7/6/07
44	**FINISHES AND FIXTURES**	**16 days**	**Fri 6/1/07**	**Tue 6/26/07**
45	Drywall	9 days	Fri 6/1/07	Fri 6/15/07
46	Paint	4 days	Fri 6/15/07	Thu 6/21/07
47	Install Door Finish Hardware	1 day	Thu 6/21/07	Fri 6/22/07
48	Plumb Trim	2 days	Thu 6/21/07	Mon 6/25/07
49	HVAC Trim	2 days	Thu 6/21/07	Mon 6/25/07
50	Electrical Trim	2 days	Thu 6/21/07	Mon 6/25/07
51	Final Cleaning	1 day	Mon 6/25/07	Tue 6/26/07
52	SUBSTANTIAL COMPLETION INSPECTION	0 days	Tue 6/26/07	Tue 6/26/07
53	**PROJECT FINALIZATION**	**16 days**	**Tue 6/26/07**	**Mon 7/23/07**
54	Punch List Items	10 days	Tue 6/26/07	Thu 7/12/07
55	Demobilization	1 day	Thu 7/12/07	Fri 7/13/07
56	O. & M. Manuals and As-built Drawings	5 days	Mon 7/16/07	Mon 7/23/07
57	Occupancy Permits	5 days	Mon 7/16/07	Mon 7/23/07
58	Building Acceptance and Completion	0 days	Mon 7/23/07	Mon 7/23/07

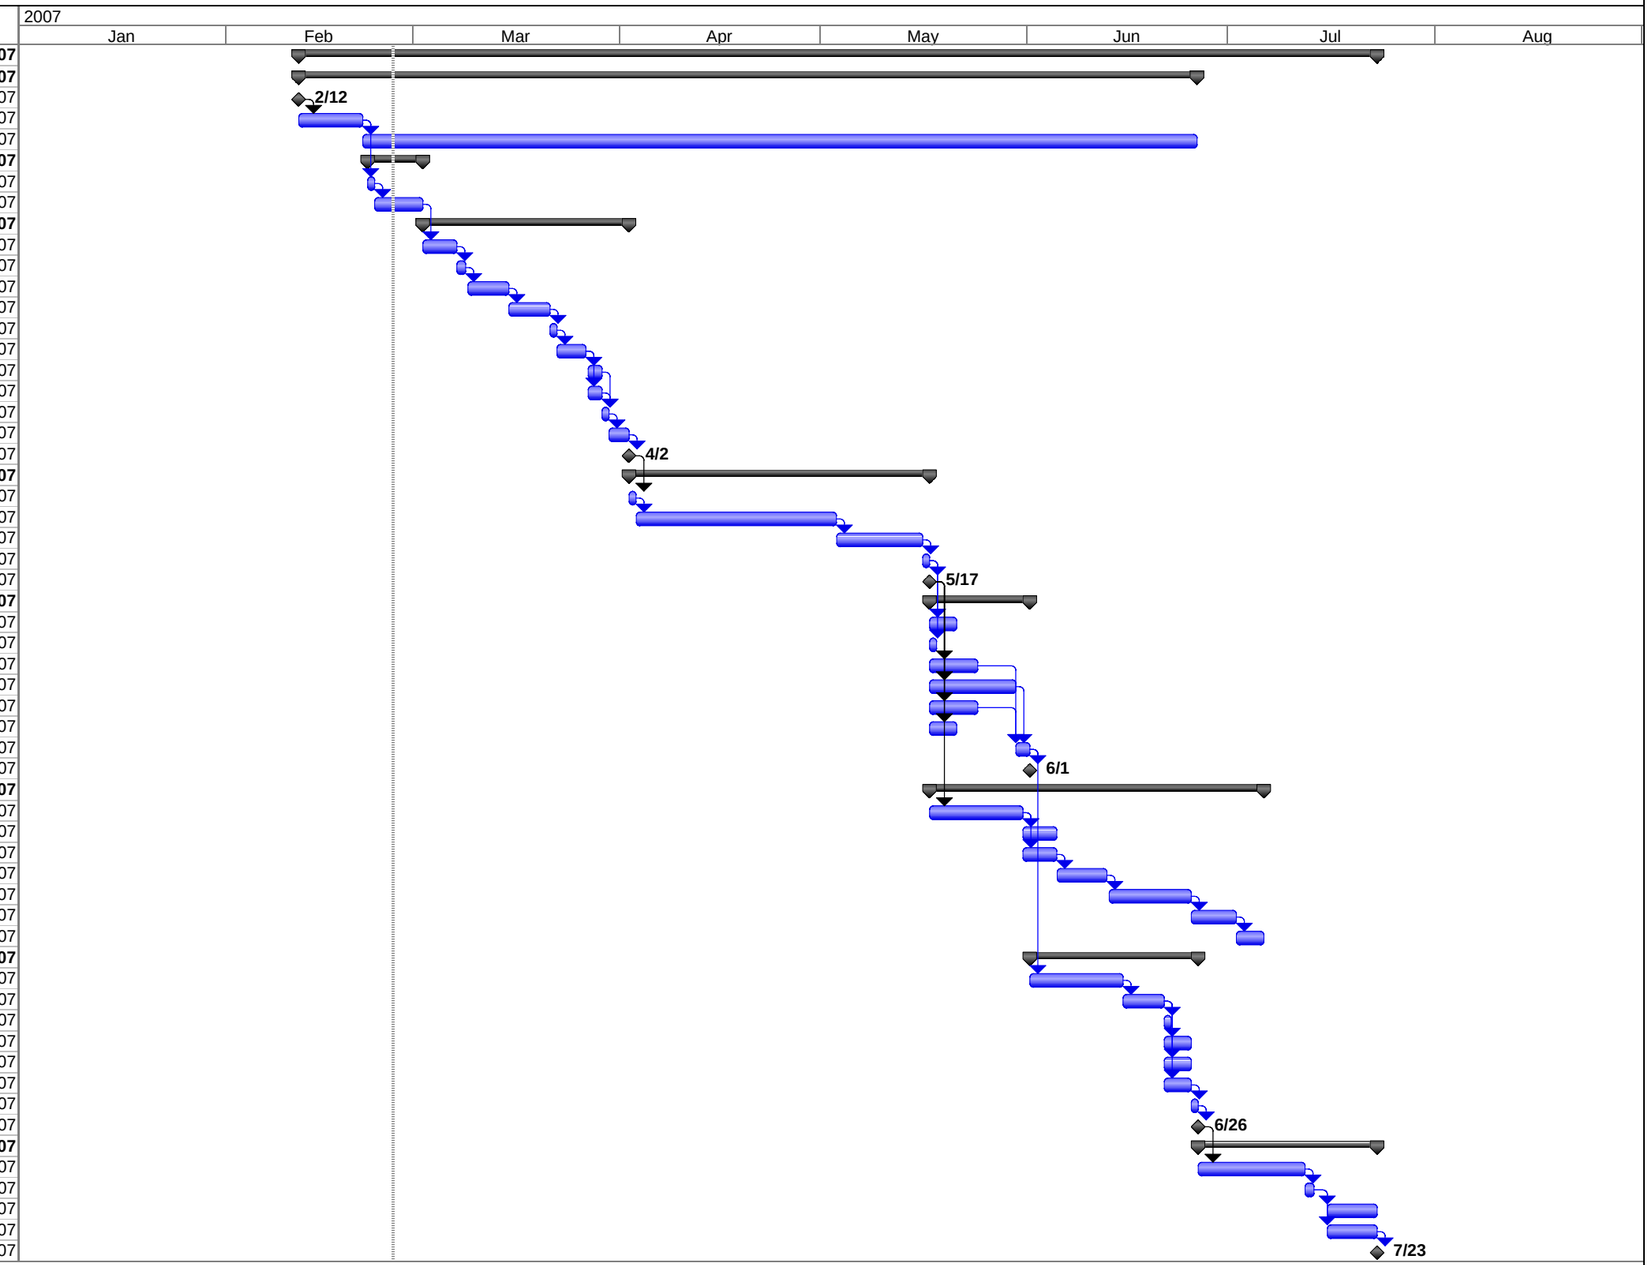

Project: Jones Construction- Lake Cit
Date: Mon 2/26/07

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone
